AI-Powered Project Tracking Report

Automatically generated visual summary of project tracking datasets.

AI Summary

Here’s a concise project-management summary across the available datasets:

Overall picture
The portfolio shows **active execution with meaningful delivery risk**:
- Tasks are mostly progressing, but there is a **material overdue and blocked workload**.
- Milestones are slipping on average, with some large delays.
- Issues/risks are frequent and often carry non-trivial schedule impact.
- Resource allocation shows both **over-allocation and underutilization**, indicating planning imbalance.
- Notifications are being generated, but many appear **unacknowledged**, which can weaken escalation response.

Key issues by area

1) Task execution and schedule health
- In `tasks.csv`, most tasks are not overdue, but there is still a significant overdue portion:
- **1,510 of 1,800 tasks are not overdue**, implying **290 overdue tasks**.
- Task slip is mixed:
- Average slip is slightly negative overall, but the distribution includes delays up to **22 days**.
- Task statuses include **Blocked** and **Not Started**, which suggests some work is not moving as planned.
- Risk scores are moderate overall, but some tasks are clearly high-risk.

Meaning: Delivery is not failing broadly, but there are enough delayed and blocked tasks to threaten downstream work, especially where dependencies exist.

2) Milestone delays
- Milestones show an average slip of about **2.6 days**.
- The maximum milestone slip is **42 days**, which is a major schedule concern.
- Since milestones represent key control points, even a small average delay can hide serious slippage in critical phases.

Meaning: The schedule is under pressure at the control-point level, and some projects may be absorbing delay without yet fully recovering.

3) Issues and risks
- `issues_and_risks.csv` shows:
- Severities range from **Minor to Severe**
- Statuses include **Open, Investigating, Mitigating, Closed**
- Estimated schedule impact averages about **4.5 days**, with a maximum of **21 days**.
- Common issue types include operational risks such as **supplier delay, capacity constraint, tooling, and test failure**.

Meaning: The portfolio has active risk exposure, and several issues have enough schedule impact to affect milestone dates if not actively managed.

4) Resource allocation
- `resource_conflicts.csv` shows average allocated hours of about **185 hours/month**.
- The range is wide, from **81 to 260 hours/month**, which indicates uneven workload distribution.

- Allocation statuses include **Underallocated**, **Balanced**, and likely overloaded categories such as **Critical/High**.

Meaning: Some people are likely overloaded while others have spare capacity, which can create bottlenecks in critical roles and reduce overall delivery efficiency.

5) Notifications and communication
- Notifications are generated for:
- **Task Overdue**
- **Milestone Slip**
- **Resource Conflict**
- **High Risk Score**
- `acknowledged` is present but many notifications are **False**, meaning they were not acknowledged.
- Urgency includes **FYI, Escalation, and Action Required**.

Meaning: The platform is detecting problems, but response discipline may be weak. If alerts are not acknowledged, issues can persist longer than they should.

Practical next steps for the project manager
1. **Review the top overdue and blocked tasks first**
- Focus on tasks with high priority, high risk score, or dependency chains.
- Clear blockers or reassign owners where progress has stalled.

2. **Triage milestone slips over 7 days**
- Investigate milestones with the largest delays, especially those tied to critical path work.
- Confirm whether recovery actions are in place and realistic.

3. **Escalate major/severe open issues**
- Prioritize supplier delay, capacity constraint, and test failure risks.
- Ensure each has a named owner, mitigation plan, and due date.

4. **Rebalance resource allocation**
- Move work from overloaded people to underallocated team members where skills allow.
- Pay special attention to critical roles on late projects.


5. **Improve notification follow-up**
- Require acknowledgment for escalation and action-required alerts.
- Track repeat unacknowledged alerts as a management KPI.

6. **Use risk score and slip together**
- Don’t rely on status alone.
- A task or milestone with moderate progress but high risk score may still need intervention.


Bottom line
The portfolio appears **operationally active but not fully stable**. The main concerns are **overdue tasks, milestone slippage, active issues with schedule impact, and uneven resource loading**. The biggest management opportunity is to **tighten escalation and reallocate capacity early**, before delays cascade into more milestone misses.

Dataset: Project_Data/issues_and_risks.csv

Issue count by severity

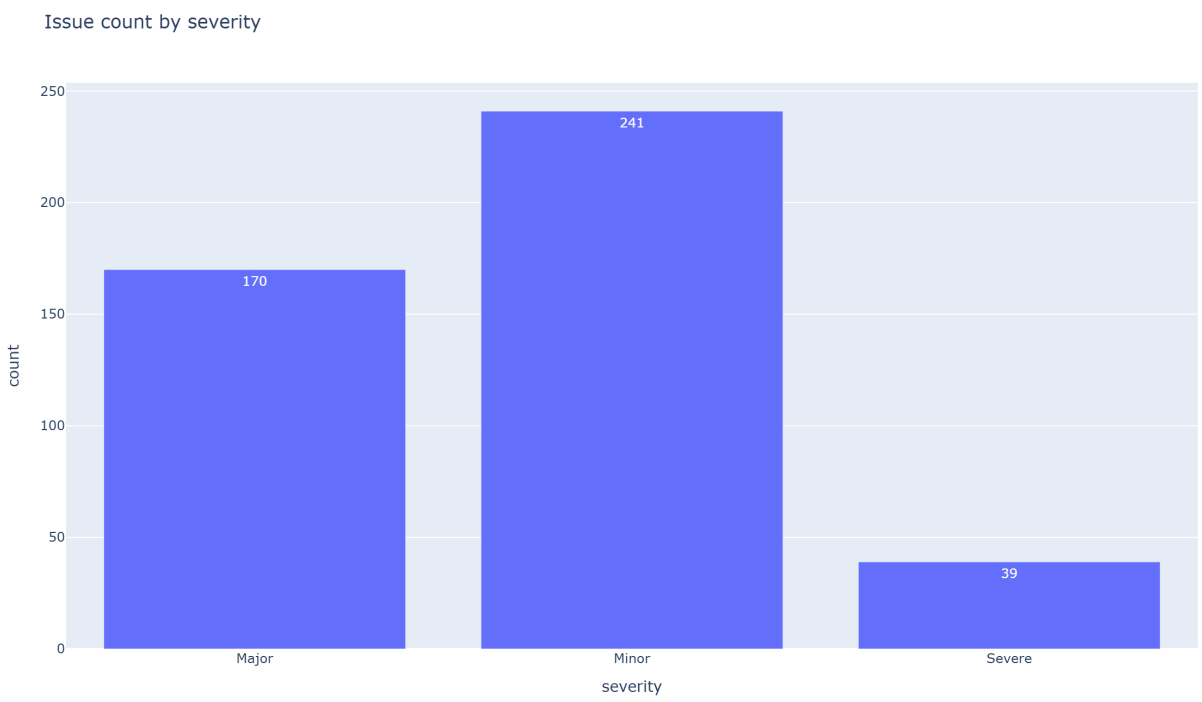


Issue count by status

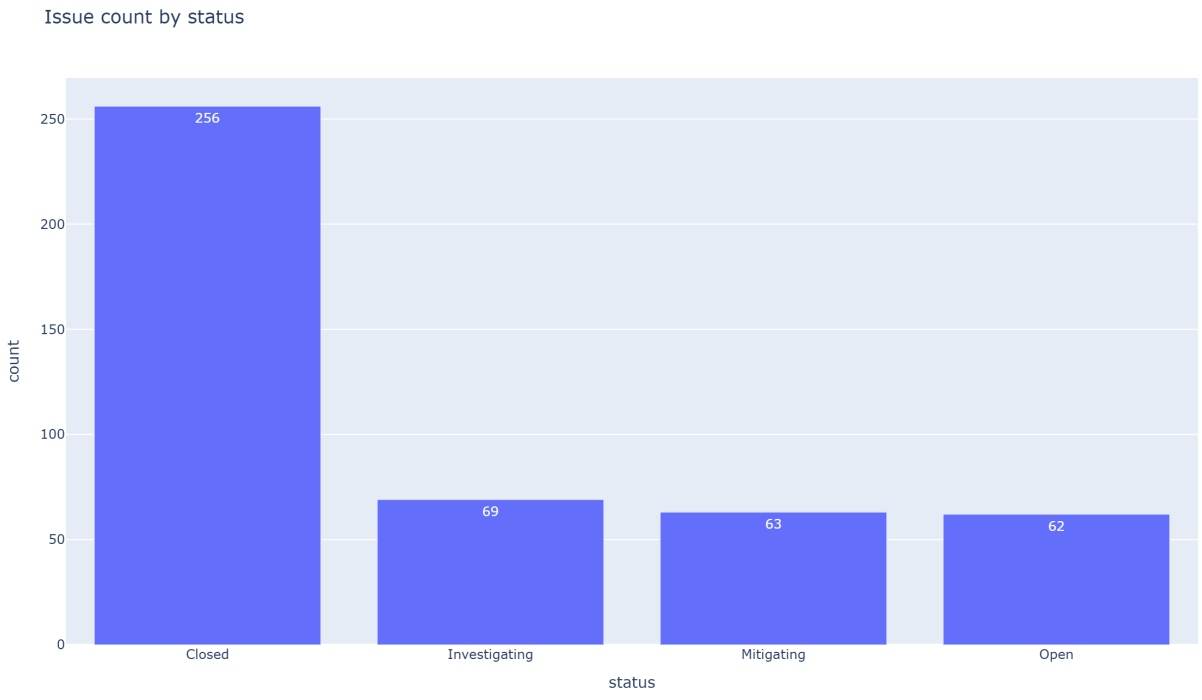


Dataset: Project_Data/milestones.csv

Average milestone slip by team

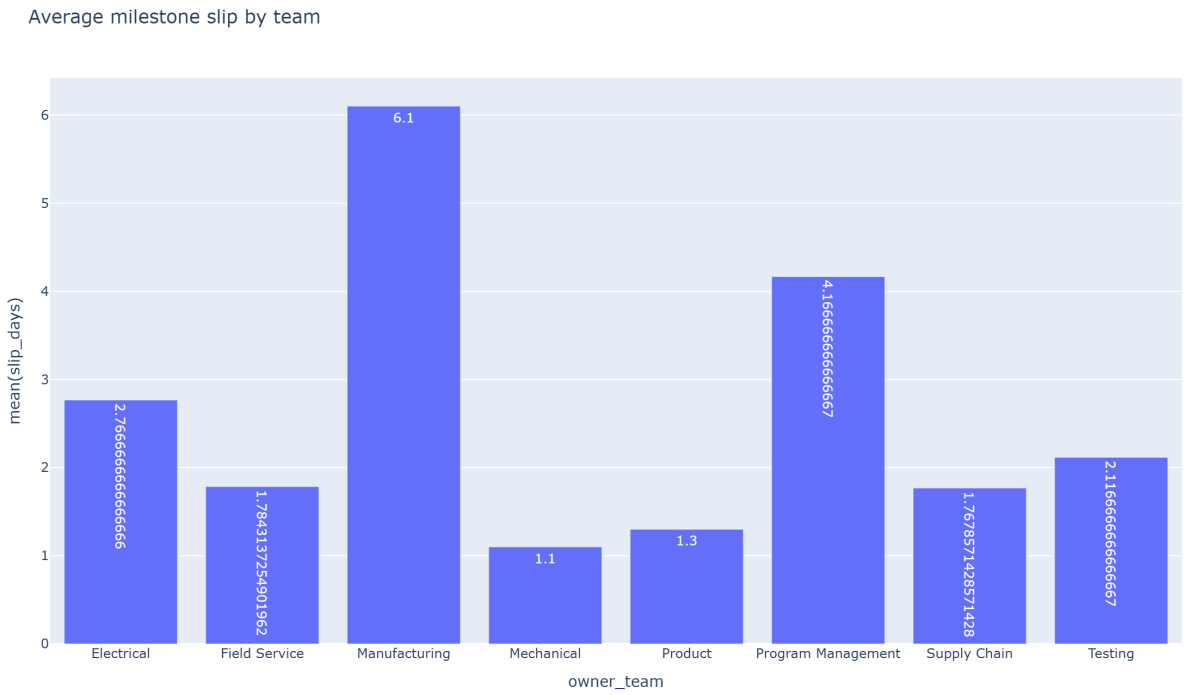


Average milestone slip by achievement status

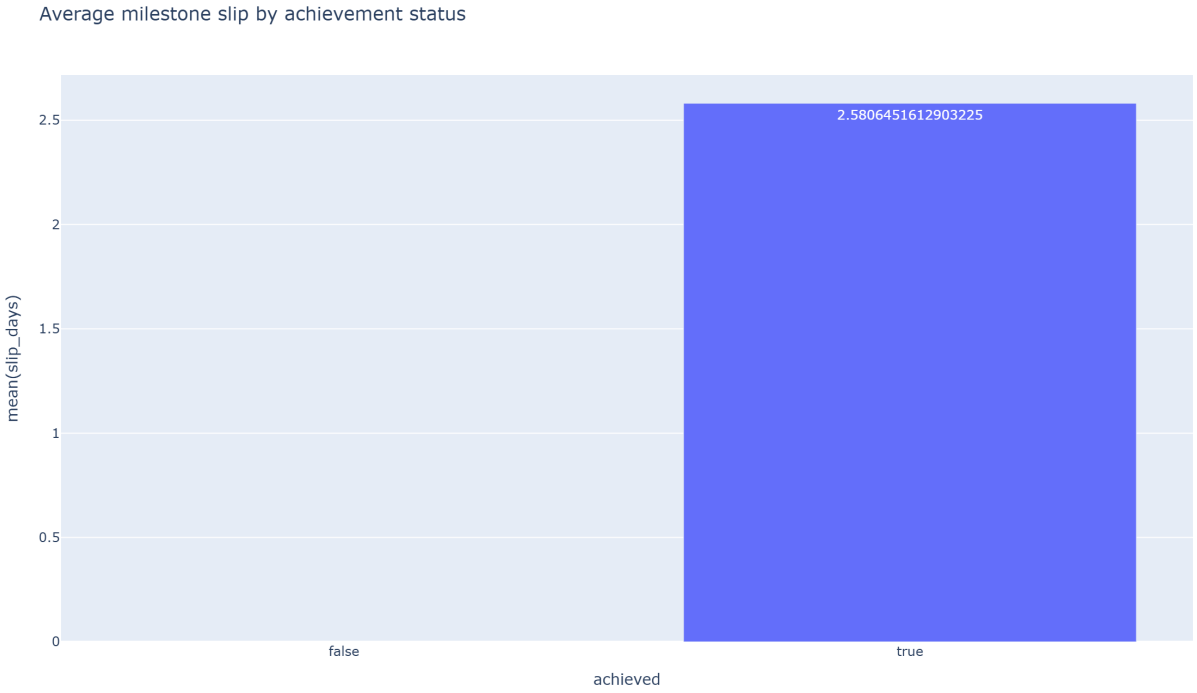


Dataset: Project_Data/notifications.csv

Notification count by urgency

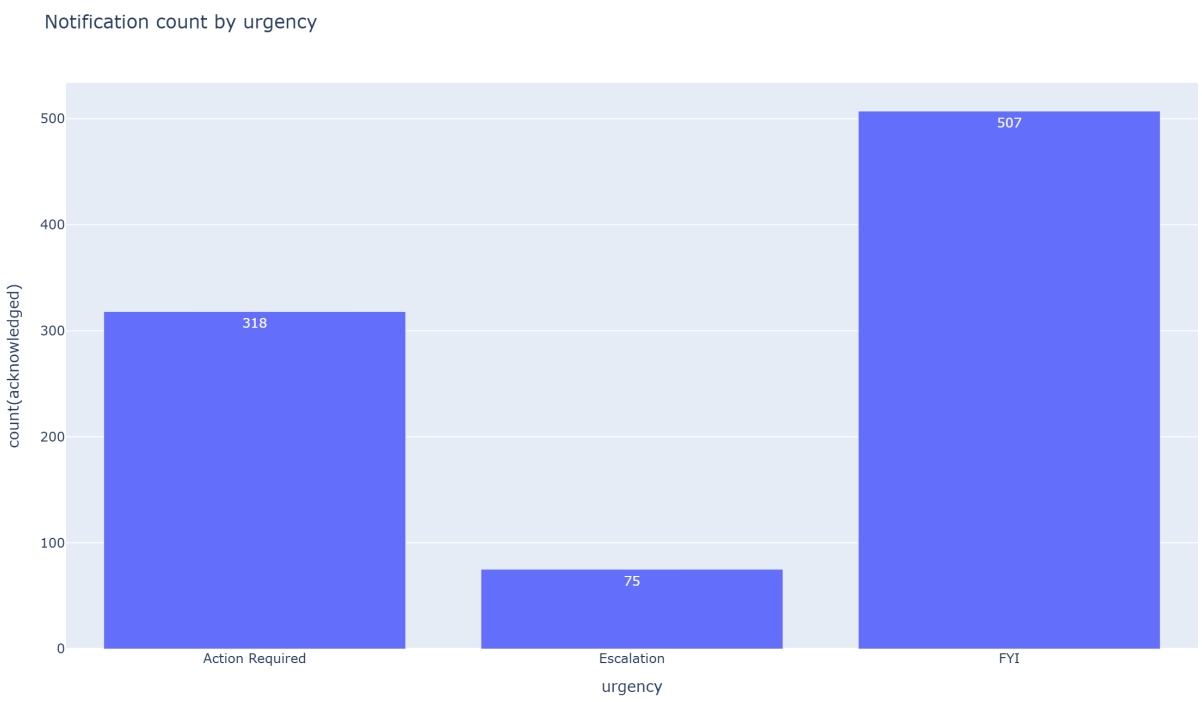


Notification count by trigger type

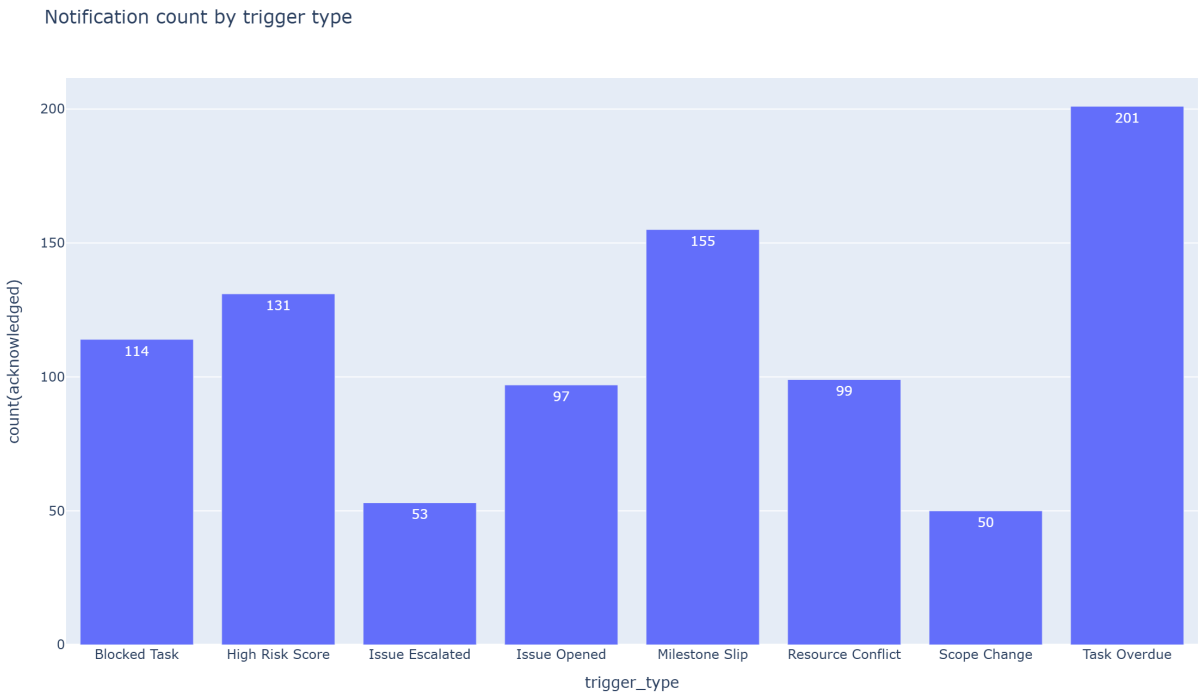


Dataset: Project_Data/people.csv

Average FTE by team

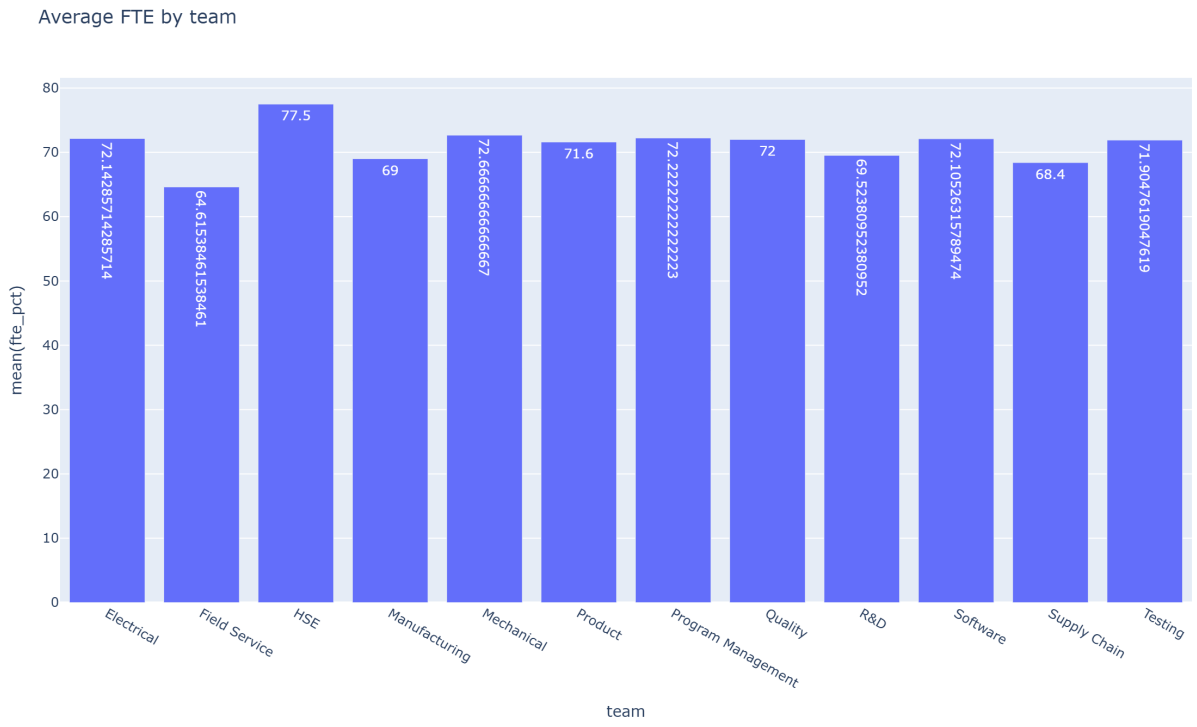


Average FTE by role

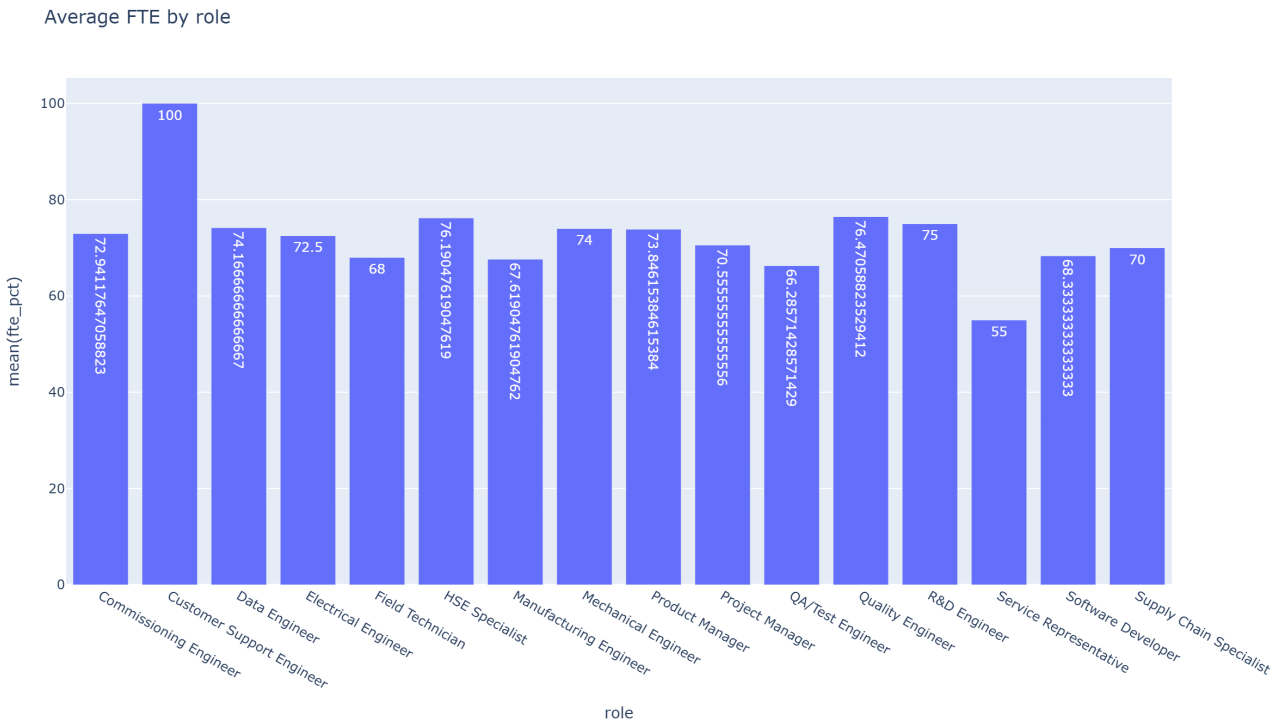


Dataset: Project_Data/planner_export_like.csv

Task count by progress

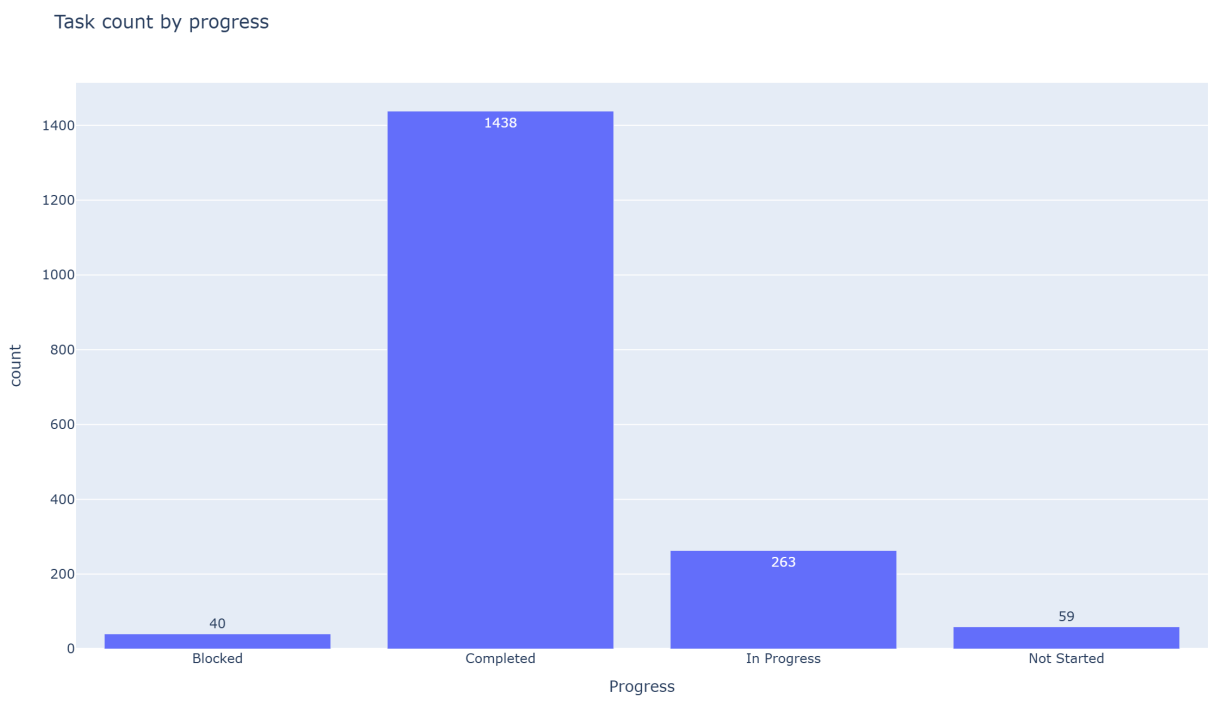


Average percent complete by priority

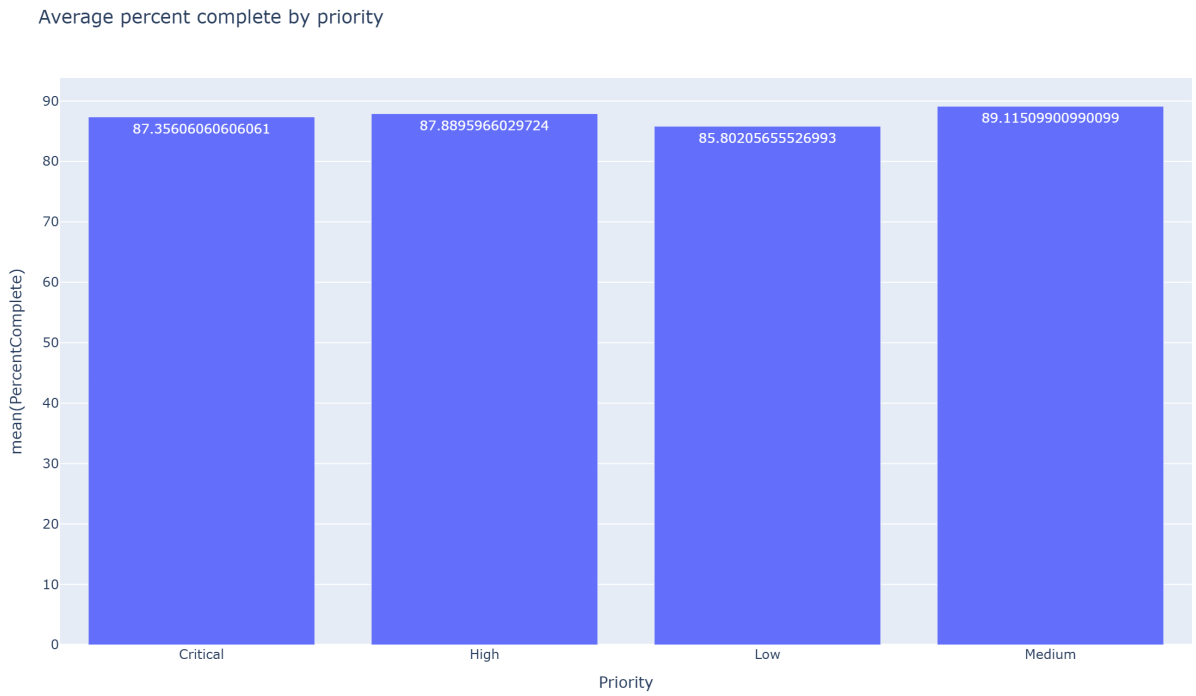


Dataset: Project_Data/projects.csv

Average budget by project complexity

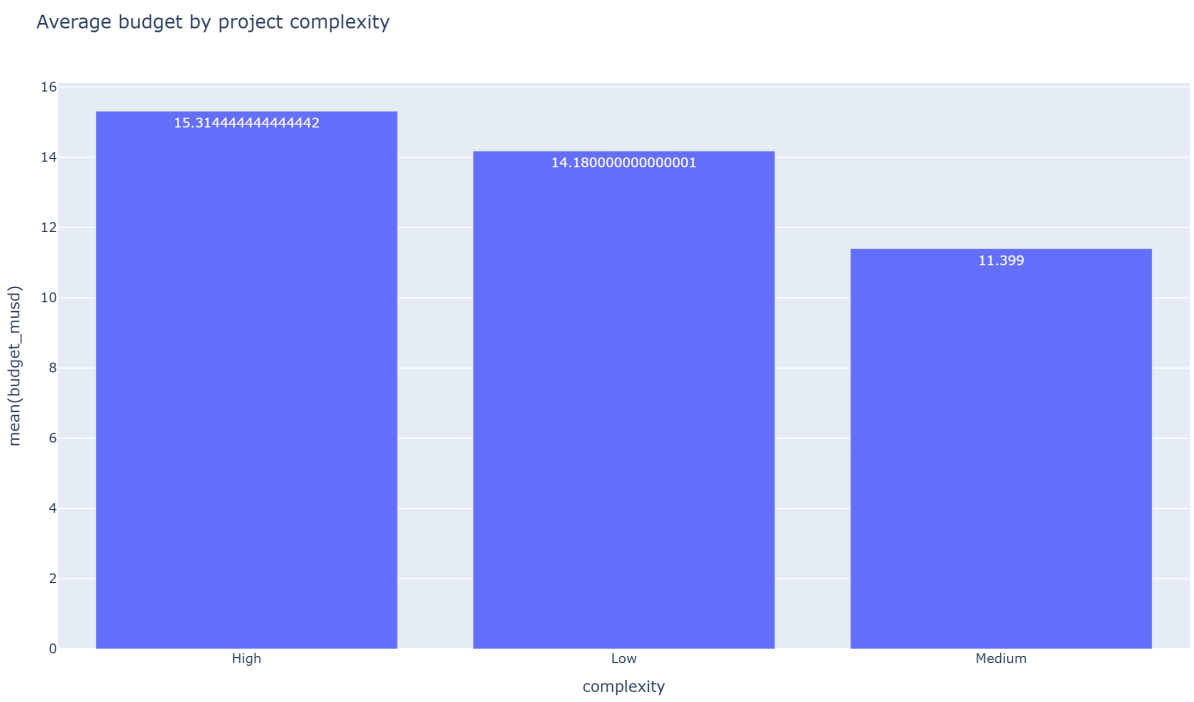


Average budget by region

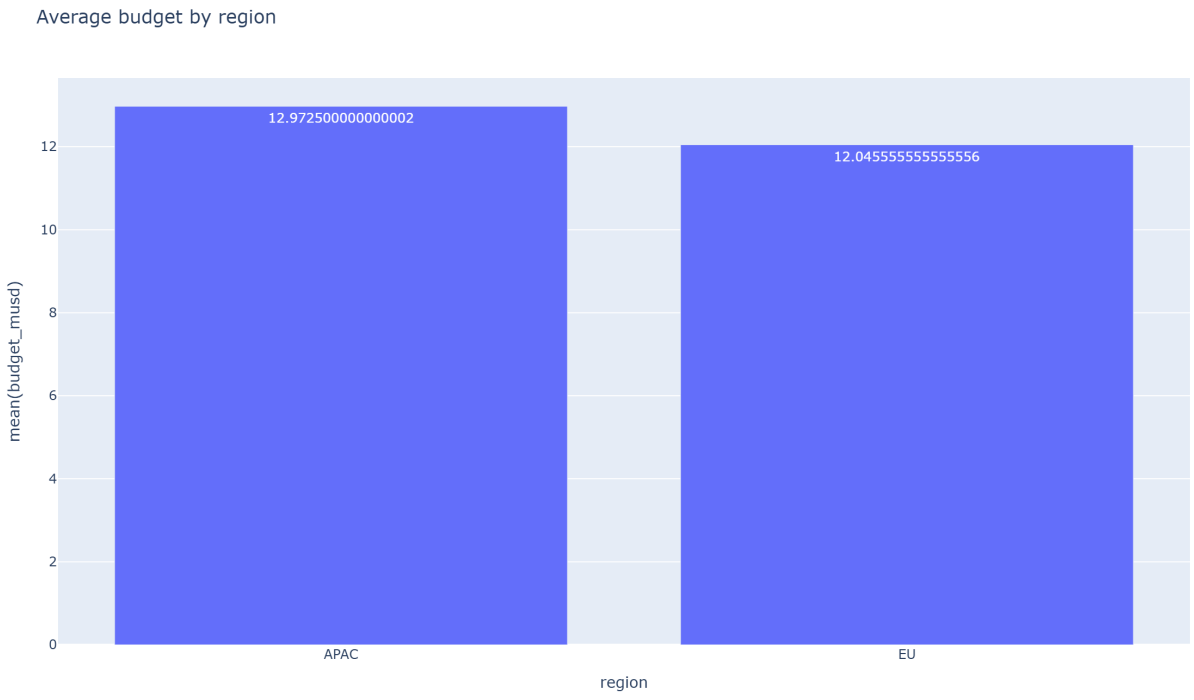


Dataset: Project_Data/resource_conflicts.csv

Average allocated hours by allocation status

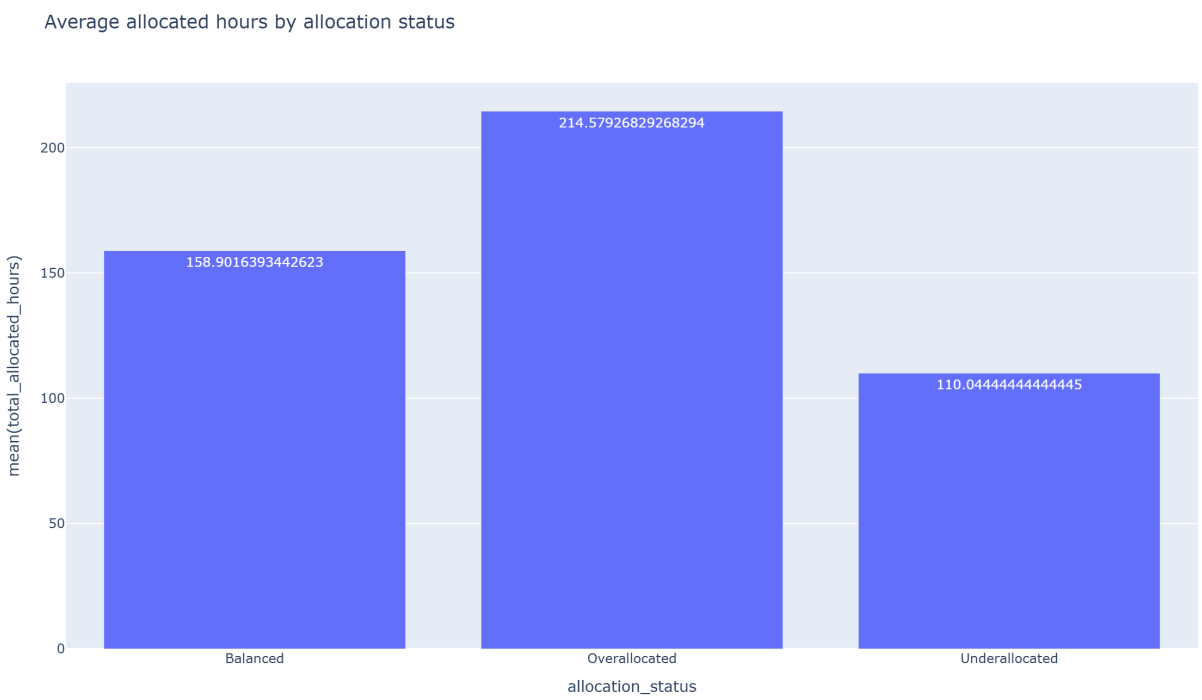


Average allocated hours by conflict severity

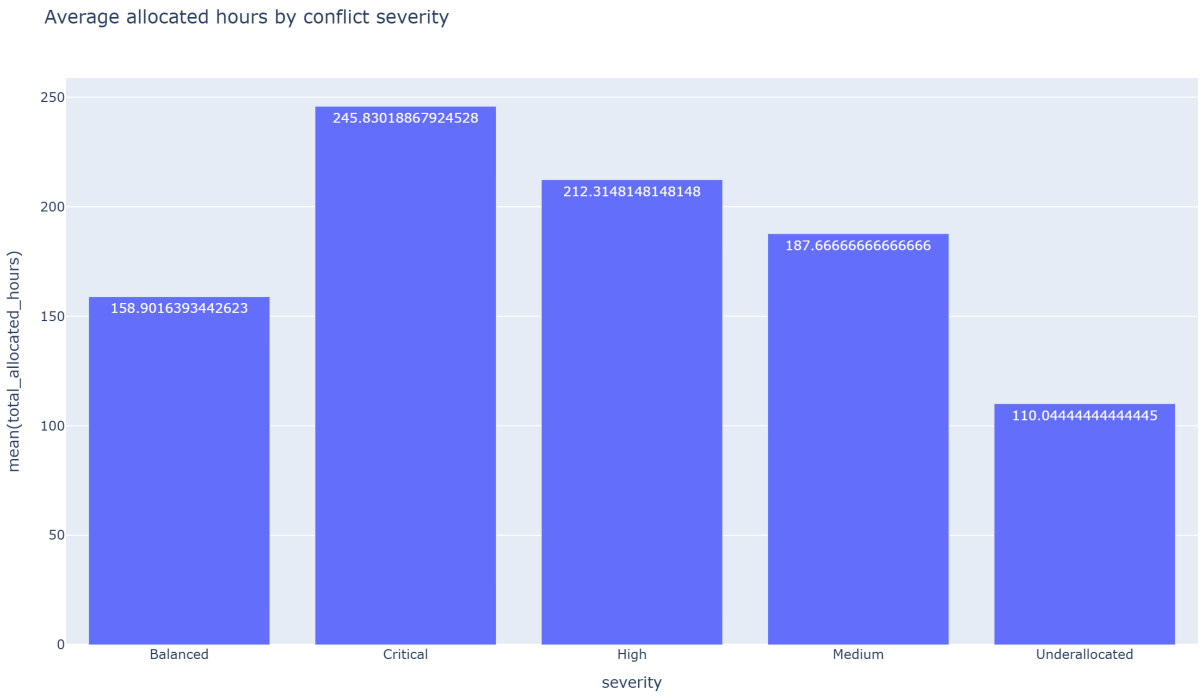


Dataset: Project_Data/tasks.csv

Task count by status

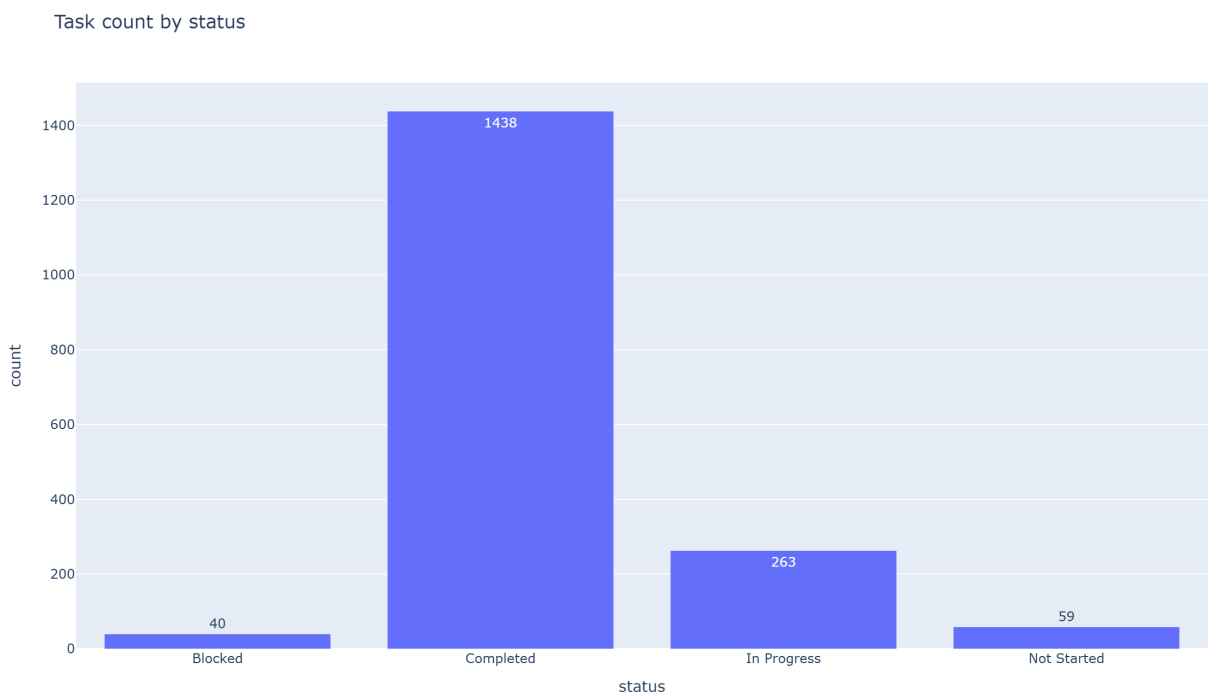


Overdue task count by priority

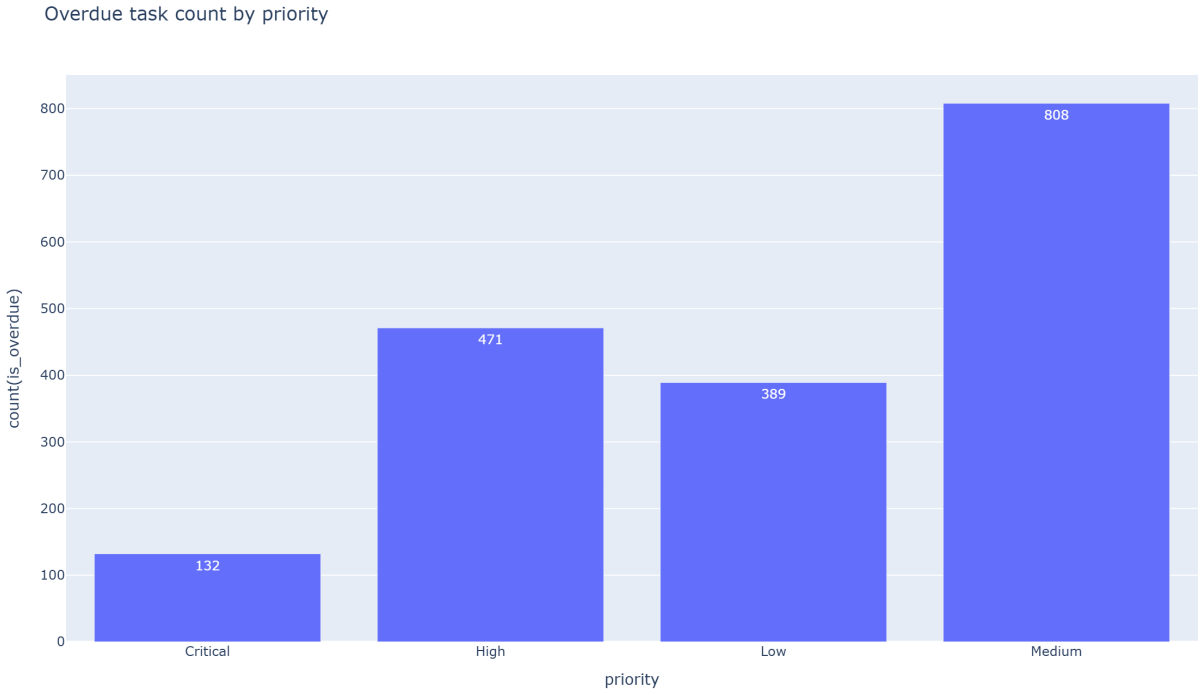

Dataset: sample2.csv

Total sales over time

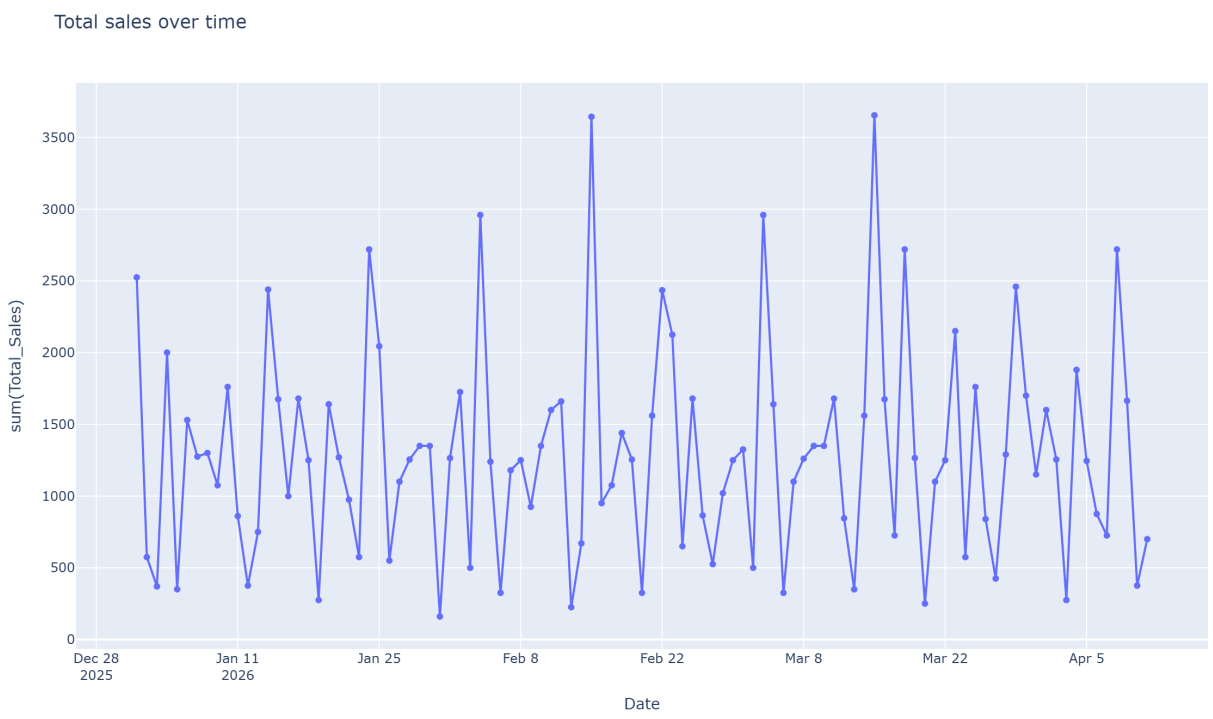

Total sales by region

